

Course: Individual Software Development Process' 2026

*Iteration Report: **Iteration 1***

By **Wassawin the Goat of All Time (W-GOAT)**

Chosen Irl Challenge: Project B: Lab Workflow & Request Management



Kantinan Lertluckpreecha	6810545476
Jedsada Ungsunantwiwat	6810545522
Pathadon Aougsk	6810545808
Wassawin Swangjaeng	6810545905
Siraphob Phonphakdee	6810545930

Table of Contents

1. Project Snapshot.....	1
1.1 Project-Wide Gantt Chart.....	1
1.2 Current Iteration Gantt Chart.....	1
2. Sprint/Board Status Snapshot.....	2
3. Scope Addition/Change Log.....	3
4. Retrospective.....	3
5. Testing & Quality Notes.....	3
6. Project Risk Register.....	4
7. Individual Contribution Log.....	5


1. Project Snapshot

Note: This section must include both Gantt Chart for the whole project and the calculation of the critical path for the project, and each iteration. Created via Plane.so.

Note: Project Repository is mandatory for the report submission of Iteration 2. For Iteration 1, this can leave blank as “(WIP)”.

Project Repository: <https://github.com/PathadonAougsk/ISP>


1.1 Project-Wide Gantt Chart

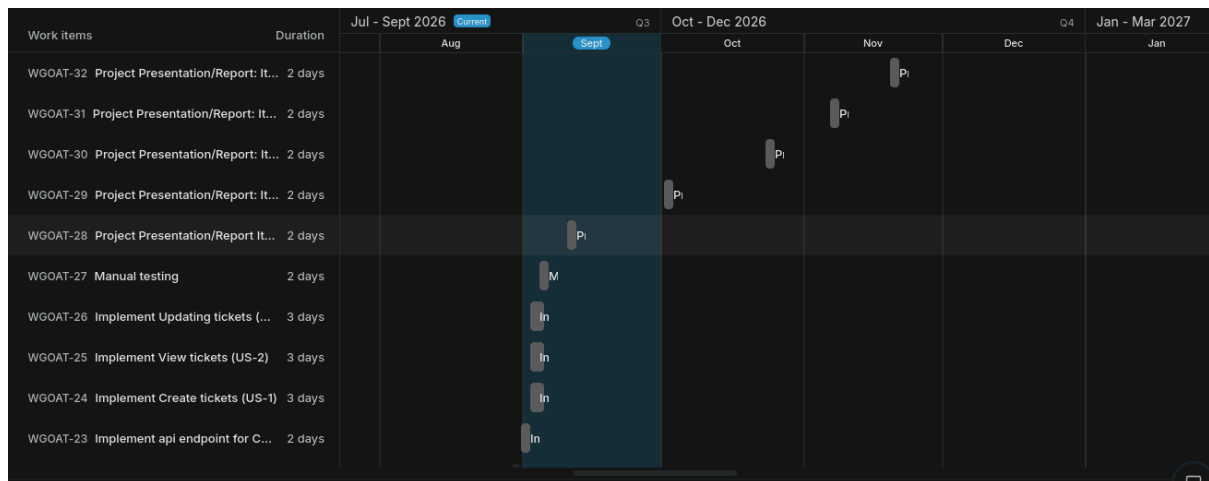

Critical Path: Architecture/DB schema finalization → Tickets Create implementation (US-1) → Tickets update implementation (US-2) → Tickets delete implementation (US-3) → Ticket module → Deployment

Critical Path Duration: 83 calendar days

1.2 Current Iteration Gantt Chart

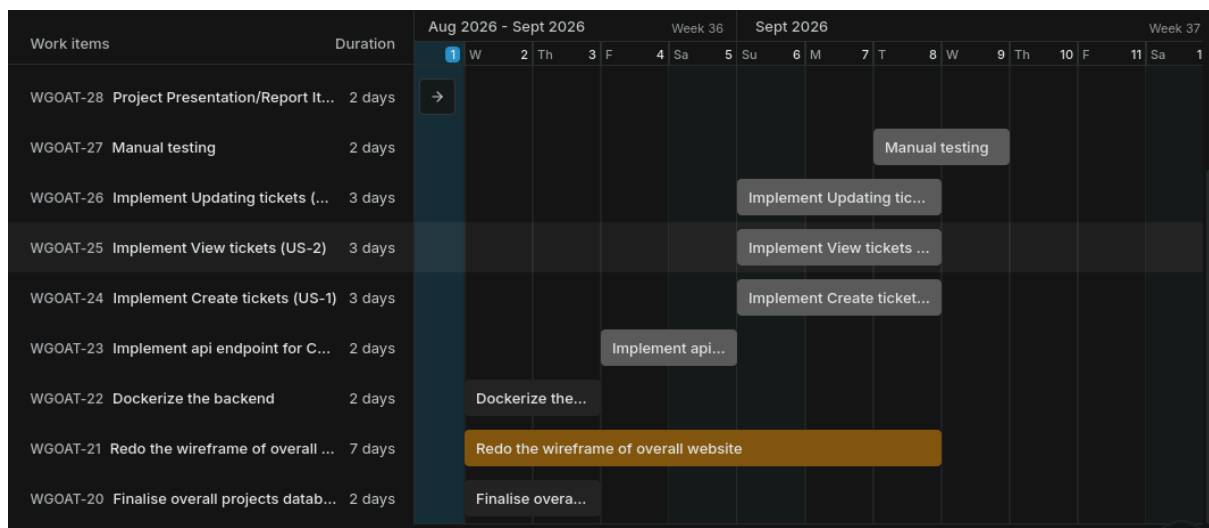

Critical Path: Finalize overall Project model → Implement Api endpoint → Implement Create ticket (US-1) → Implement View ticket (US-2) → Implement Update ticket (US-3)

Critical Path Duration: 7 calendar days

2. Sprint/Board Status Snapshot

Note: User Stories Must Be Consistent User Stories in Software Proposal (Week 4). For Maximum Capacity, It Must Be:

- 3 User Stories for Iteration 1
- 4 User Stories for Iteration 2

Iteration Goal: Deliver working lab tickets so Lab Members can submit new tickets, view and track the status of their own tickets, and update tickets assigned to them, directly supporting US-1, US-2, and US-3 from the SRS.

Capacity Declared: 3 user stories (at the Iteration 1 hard limit; no basis needed as this is the fixed ceiling for a first iteration).

User Story	Description	Owner	Status	Within Capacity (Y/N)	Notes
US-1	Lab Member submitting new lab tickets.	Siraphob Phonphakdee	Not Started	Y	Blocked on API; no create endpoint yet
US-2	As a Lab Member, I want to view and track my tickets.	Kantinan Lertluckpreecha	Not Started	Y	Blocked on API; no read endpoint yet.
US-3	As a Lab Member, I want to update the assigned tickets with additional information or status.	Pathadon Aougsk	Not Started	Y	Blocked on API; no update endpoint yet. Role-based validation deferred to Iteration 2.

3. Scope Addition/Change Log

Note: Log any item added, expanded, or swapped in after planning began. Empty is a good sign; frequent entries signal scope creep.

Item added/changed	Reason	What as dropped to compensate (one-in-one-out)
Containerise deployment with Docker	Using bare metal complicated the process of setting up, maintaining, and deploying.	Role-based validation on US-3 deferred to Iteration 2.

4. Retrospective

What went well	What didn't go well	Action items for next sprint
Drafted backend on FastAPI with Supabase, ready for endpoint work in Iteration 2.	No API Endpoints were written. So all three user stories are now stuck.	Implement ticket creation, reading, and update endpoints first.
Dockerize the frontend and backend.	Rushed the UI/UX design without prior planning via sketching, and went straight to prototyping in Figma.	Reserve a fixed UI-polish buffer in future sprint planning rather than treating it as leftover time.

5. Testing & Quality Notes

Note: any bugs, defects, tests (informal & formal) encountered and/or fixed during this iteration can be included here. If there is none, just put "(None applicable)" below.

There were some obstacles during this iteration. At first, we designed the UI without proper requirements or design rules, which resulted in a poor and inconsistent wireframe in Version 1. Therefore, we decided to create design requirements, such as the font family, UI style, and color palette. As a result, the design was better and more consistent than Version 1.

Then, we brainstormed and questioned different aspects of our UI design, such as: "What does this button do?" "Why is this widget placed here?", and "How can we use the space more efficiently?" Through this process, we polished the UI layout as much as we could and moved on to the backend/API implementation in Iteration 2.

6. Project Risk Register

Risk ID	Description	Likelihood (L/M/H)	Impact (L/M/H)	Mitigation/Contingency	Status
R-01	Data model may need rework if later iterations add progress notes (SRS-5), announcements (G-0), or attachments, none of which the current schema supports	M	H	Keep the ticket schema loosely coupled; add new features as separate tables with FKs to ticket rather than extending it with columns	Monitoring
R-02	Only one member has prior development experience, so Iteration 2 self-declared capacity may be miscalibrated.	M	M	Track actual completion time per story this iteration to build a velocity baseline for future planning	Open
R-03	Only one member has Docker experience, and only basic containerisation; no reliable owner.	M	H	Pair that one member with another member on container work; keep bare-metal run steps in the README as fallback.	Open

7. Individual Contribution Log

Note: One row per member, filled in by that member. The submission of this file considered that the form below is consented and confirmed by the whole team. This section directly supports the Individual Project Contribution and Peer Evaluation grading components.

Note 2: For Iteration 1, evidence can be a reference to the video presentation/iteration report that is related to the responsible task(s) (e.g. Lalita's Evidence). However, for Iteration 2, the reference must be on **GitHub** file and commit only, which is uploaded by that team member.

Student Name	Tasks owned this sprint	Course concept(s) applied	Evidence	Self-rated effort (1-5)
Kantinan Lertluckpreecha	Designing the Tickets page, discussing Tasks and Tickets back-end workflows, and contributing to web layout and color-palette decisions.	Scope management and KAOS during the back-end discussions to balance requirements with practical implementation.	File's editing history in Figma, Segment 2 and 4 in the presentation video.	5
Jedsada Ungsunantwiwat	Design the UX/UI for the login page	Design phase of the SDLC identifying visual elements/component s needed before build work	File's editing history in Figma Segment 4 in presentation video	5
Pathadon Aougsk	Scaffolded the backend and frontend in preparation for US-3 implementation while also dockerizing it.	Apply knowledge about the development environment to lead to the conclusion of using Docker.	https://github.com/PathadonAougsk/ISP Commit 19d9038	5
Wassawin Swangjaeng	Design the Dashboard and Task Table UI, and select the font family, color palette, and UI style. Editing iteration 1 presentation video	Use S.M.A.R.T. criteria to establish clear rules and requirements for the UX/UI design	- File's editing history in Figma - Segments 4, 5 in the presentation video - docs/5. Testing & Quality Notes	5
Siraphob Phonphakdee	Design of the app's theme, colors, typography, and overall feel. Reviewed each team member's page, providing feedback on improvements and iteration.	Applied SCRUM to break each design work into smaller workable chunks for everyone on the team.	docs/gantt_iteration1.png	5
